

Field Observation Report #11

Date:	<u>November 7, 2013</u>	Project:	<u>Burleigh County Shop</u>
Time:	<u>2:45 pm</u>	Project No:	<u>12-04</u>
Weather:	<u>Sunny</u>	Location:	<u>Bismarck, ND</u>
Temperature:	<u>35 degrees</u>		
% Complete:	<u>43% Visible</u>		
Trades:	<u>Masonry Work</u>		
Crew Size:	<u>5-8</u>		

The following information is a documentation of observations and findings as a result of a visit to the construction site. Items and decisions made within this reports are considered a part of the contract documents.

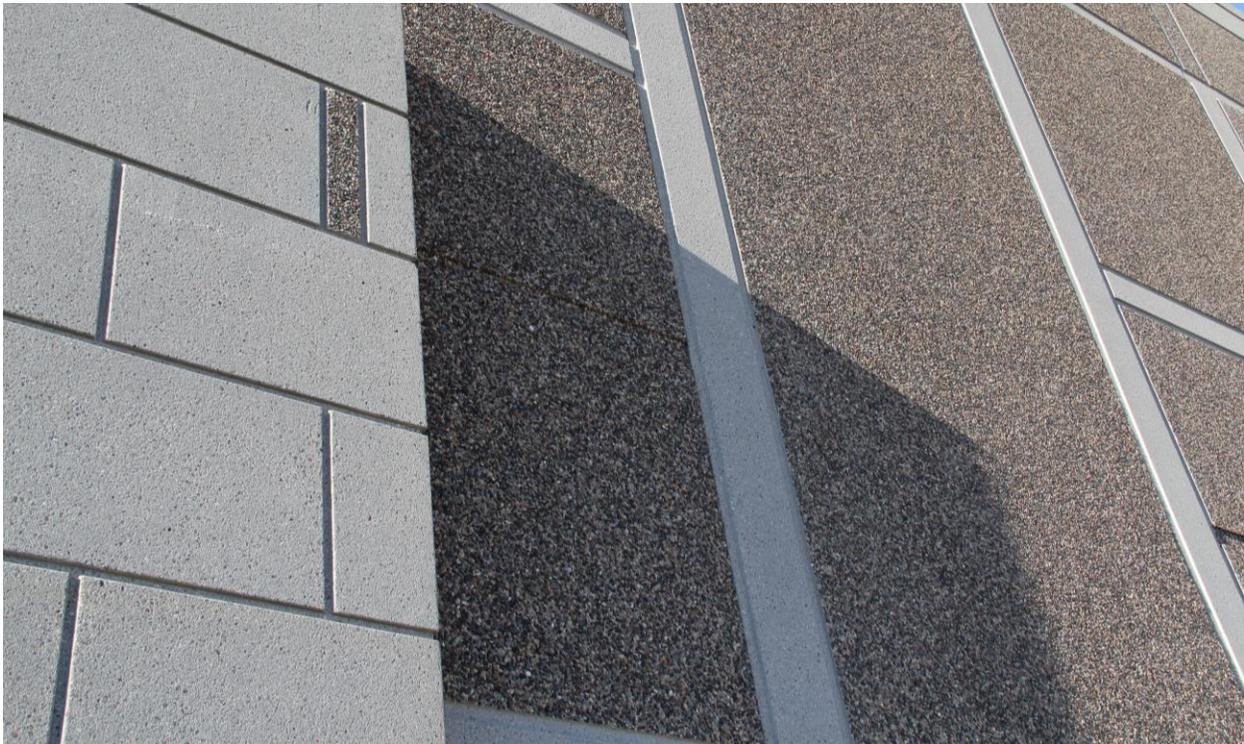


Photo 1: Transition between tall shop space and the lower administration area pre-cast panels.

1. Additional pre-cast panels have been placed; if weather cooperates, the remaining panels could be installed in two weeks' time. Several administration area panels have been placed as well. The estimated date of enclosure is the first of January 2014. (please see photo 1 & 2).



Photo 2: block veneer support angles and rigid insulation has been placed along part of the south elevation.

2. The steel roof/floor members and some deck has been placed in the administration area; the lower structural columns have been placed for the raised roof area at the administration hallway (*please see photo 3*).



Photo 3: Structural steel erection is underway in administration; the beams shown support the mezzanine above.



Photo 4: Surveying Bay masonry construction.

3. Masonry work continues around the surveying bay (*please see Photo 4*).

This concludes Field Observation Report #11. Please report any discrepancies to our office within 5 days.

Thank you,

Jennifer Jackson
