

## Field Observation Report #25

---

Date:	<u>August 7, 2014</u>	Project:	<u>Burleigh County Shop</u>
Time:	<u>3:00 pm</u>	Project No:	<u>12-04</u>
Weather:	<u>Partly Cloudy</u>	Location:	<u>Bismarck, ND</u>
Temperature:	<u>80 degrees</u>		
% Complete:	<u>97% Visible</u>		
Trades:	<u>Painting, Doors &amp; Casework</u>		
Crew Size:	<u>5-7</u>		

---

*The following information is a documentation of observations and findings as a result of a visit to the construction site. Items and decisions made within this reports are considered a part of the contract documents.*

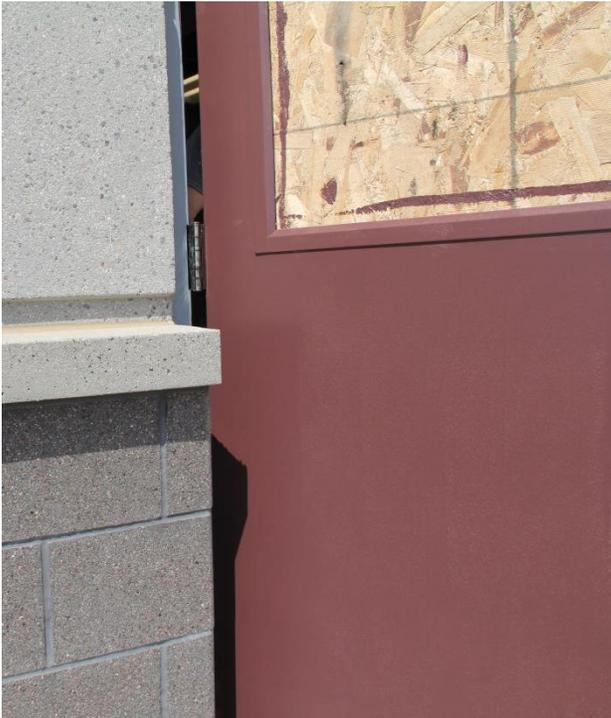


*Photo 1: Concrete Patio off of the Lunch Room has been poured*

1. The concrete sitework at the entrance and Lunch Room patio is completed. Curbs have also been poured along the front of the building.
2. Fuel storage tanks have been placed on the east side of the building.



*Photo 2: Diesel and Gas storage tanks have been placed and are in the process of being backfilled.*



*Photo 3: Exterior Doors are Painted*



*Photo 4: Raised Hallway Lighting, illuminating concrete above*



*Photo 3: Entry reception counter is being adjusted to provide storage space and accommodate computer stations*

3. Painting continues in the Shop Area. The Wash Bay epoxy painting is now complete.
4. Wooden door frames are under construction in the administration area: wood doors will be hung next week and casework is being installed in the Lunch Room & Work Room. Locker Room tile flooring is also being set.
5. The curtain wall entry doors and hardware have been installed.
6. It has been determined that part of the landscaping work will be conducted this fall and the remainder will be completed in the Spring of 2015. Cashman Nursery will provide their recommendations on how to divide the Landscaping Package to best serve the plants and sequence their work. The contract indicates a 365 day warranty on all plants starting once landscaping is complete. This will require any plants that do not survive up to Spring of 2016 to be replaced at no cost to the owner.
7. Interior pre-cast in the reception area requires cleaning.

This concludes Field Observation Report #25. Please report any discrepancies to our office within 5 days.

Thank you,

Jennifer Jackson
